

Marylebone Square

Community Update



Dear Neighbour,

We hope you are all keeping well and looking forward to the Christmas break. From the Team at Marylebone Square we would like to wish you a Merry Christmas and a Happy New year.



Our project

The works at Marylebone consist of constructing a collection of both high-end and affordable apartments over 5 storey, carefully chosen boutiques and restaurants, and a versatile community hall.

Progress update – December 2021:

Its been a year since we have commenced on site and we have reached a number of milestones from completing the piling work, erecting the top down gantry and tower cranes and the most recently the completion of the excavation works to form the basement.

We have removed over 50,000m³ from site and over 90% of this material has been diverted from landfill.

As we have started to build the structure from the basement up, the temporary propping is being removed. The main core on the south is nearly completed and the ground floor slab has commenced. The works remain on schedule.

Please email marylebonesquare@fourcommunications.com to be included in future correspondence. The next residence meeting will be on 15th December 2021 at 5.30pm

Meet the Site Team



Graham Potts
Senior Project
Manager



Dean Probert
Works Manager



Trusha Dabasia
Senior Engineer

Site Contact details :

✉ Trusha.Dabasia@kier.co.uk

Working Hours:

Monday to Friday : 08:00 to 18:00
Saturday : 08:00 to 13:00

Our Client

CONCORD
LONDON

Main construction works due to start in 2022

Main structure forming from ground floor.

Hoarding move along Aybrook Street





Kier Regional Building - London & South East


Marylebone Square – Community Update



Completion of Basement excavation



View looking South

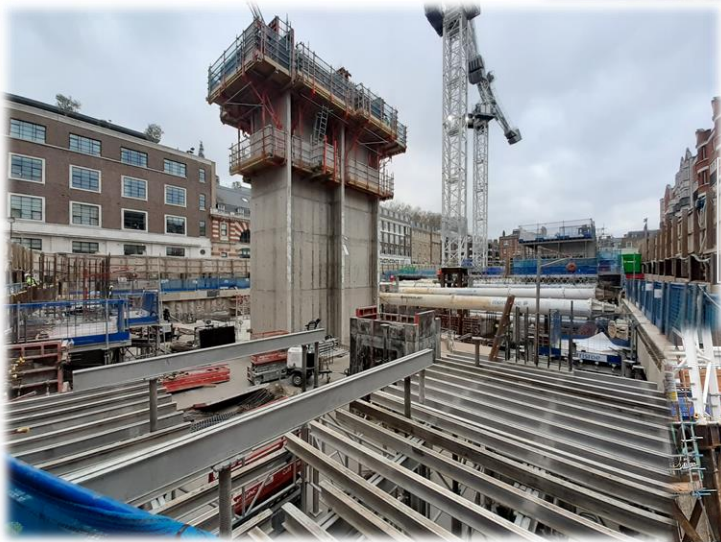

South core construction and commencing ground floor slab



Commencing north core construction



Christmas Shut down:

- 24th December 2021 to 3rd January 2022

